




WELL CONSTRUCTION LOG (UNCONSOLIDATED)

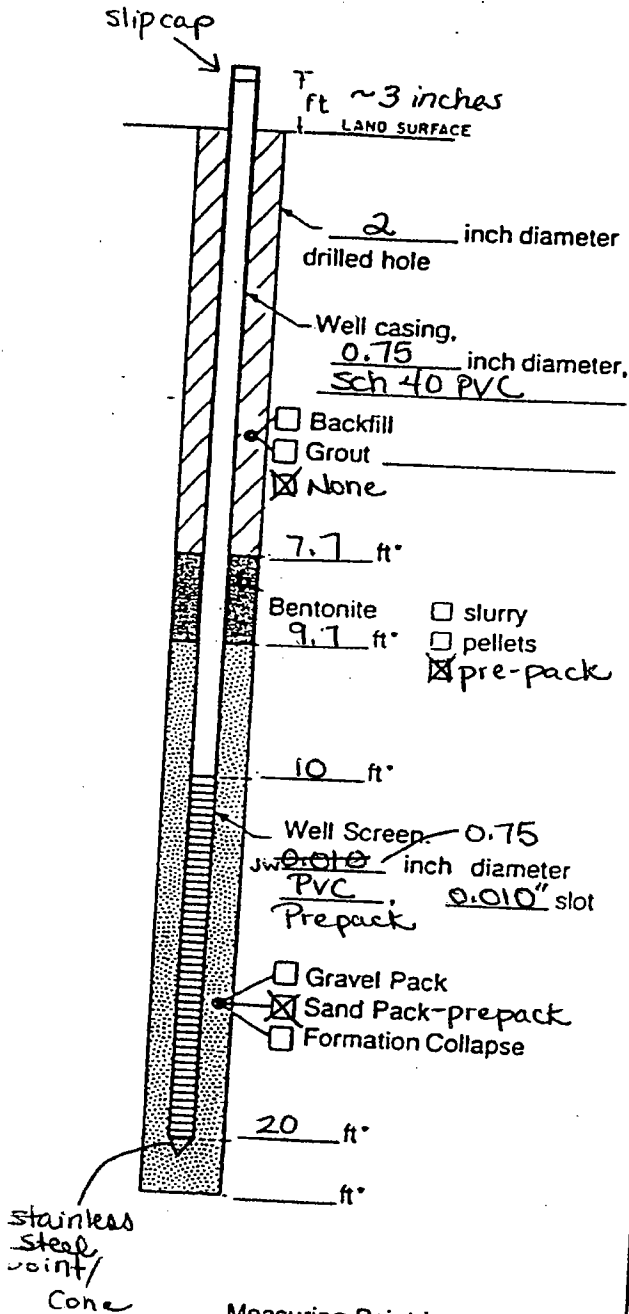

Measuring Point is
Top of Well Casing
Unless Otherwise Noted.

*Depth Below Land Surface

Project Site 35 IRZ, VAFB Well 35-MW-19

Town/City Lompoc

County Santa Barbara State CA

Permit No. _____

Land-Surface Elevation _____

and Datum 410 feet

☐ Surveyed

☒ Estimated

Installation Date(s) 9/13/00

Drilling Method SCARS direct push

Drilling Contractor Army Corps of Engineers

Drilling Fluid none

Development Technique(s) and Date(s) _____

Fluid Loss During Drilling none gallons

Water Removed During Development _____ gallons

Static Depth to Water _____ feet below M.P.

Pumping Depth to Water _____ feet below M.P.

Pumping Duration _____ hours

Yield _____ gpm

Date _____

Specific Capacity _____ gpm/ft

Well Purpose observation/monitoring

Remarks Set well in 3rd hole after 2 failed attempts. Rods would not push to total depth, therefore, installed well at 20' bgs.

Prepared by Jennifer Wiley
