Project: SAFETY-KLEEN RHONERT PARK			Log of Boring/Monitoring Well: **DMW-1**
Boring Location: 5750 COMMERCE BLVD.		Project No.: 70005-010-01	
Subcontractor and Equipment: WEEKS/MOBILE B-53		Logged By: S. McCABE	
Sampling Method: CONTINUOUS CORE	Monitoring Device: FID		Comments: DROVE PROBE BAR TO 4 FT. BGS
Start Date/Time: 2/15/95//1050	Finish Date/Time: 2/15/95//		
First Water (bgs): NA	Stabilized Water Level (bgs): NA		

Surface Elevation: NA Top Casing Elevation: NA

Sample Interval/ Recovery, Inches	Blows/foot	PID (ppm)	Depth (Feet)	Recovery	USCS Symbol	Water Level	LITHOLOGIC DESCRIPTION (color, grain size, consistency, moisture, other)
			0				8" CONCRETE OVER ROAD BASE
18/18	19		1				BLACK (5Y 2.5/1) CLAY (CL) moist, very stiff, no odor
		40	2				
18/18		15	3				
			4				DARK GRAY (5Y 4/1) SILT (ML) dry, firm, no odor
30/60							
		6	5				OLIVE (2.5Y 5/3) SILT (ML)
			6				OLIVE (2.5Y 5/3) SILTY FINE SAND (SM) wet, firm, no odor
			7				grades to coarse sand
		0	8				
			9				
			10				
			11				
			12				
			13				OLIVE (2.5Y 5/4) SILT (ML) moist, firm, no odor
			14				OLIVE (2.5Y 5/4) SILTY FINE SAND (SM) moist, firm, no odor
36/60		0	15				OLIVE (2.5Y 5/4) SILT (ML) moist, firm, no odor
			16				
			17				OLIVE (2.5Y 5/4) SILTY COARSE SAND (SM) moist, firm, no odor
			18				OLIVE (2.5Y 5/4) SILT (ML) moist, firm, no odor
			19				
			20				
			21				OLIVE (2.5Y 5/4) COARSE SAND (SP) wet, loose, no odor
			22				OLIVE (2.5Y 5/4) SANDY SILT (ML)
		0	23				No Recovery
			24				
			25				
			26				
			27				
			28				GRAY (5Y 5/1) CLAY (CL) moist, stiff, no odor
			29				
			30				

Boring Abandonment/ Well Construction Details

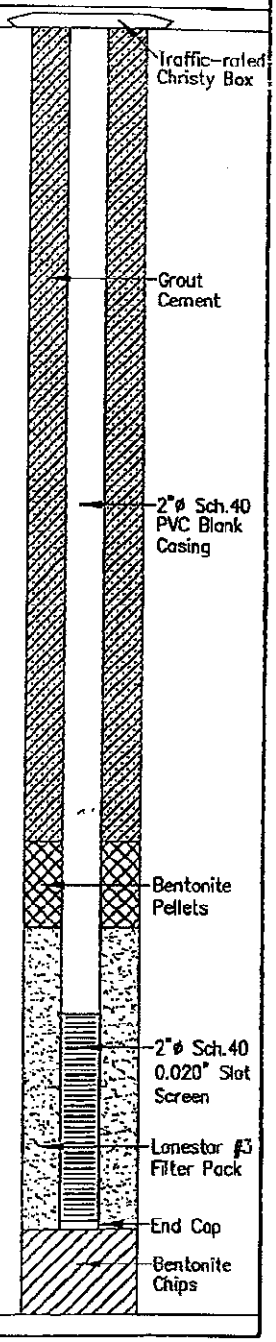

199503.201709 E:\LOGS\S-KLEEN\RHONERT\DMW-1

SECOR

Reviewed By: _____ Date: _____

Revised By: _____ Date: _____

Project: SAFETY-KLEEN RHONERT PARK		Log of Boring/Monitoring Well:
Boring Location: 5750 COMMERCE BLVD.	Project No.: 70005-010-01	DMW-1

Sample Interval/ Recovery, Inches	Blows/foot	PID (ppm)	Depth (Feet)	Recovery	USCS Symbol	Water Level	LITHOLOGIC DESCRIPTION (color, grain size, consistency, moisture, other)	Boring Abandonment/ Well Construction Details
			30					
		100	31					Bentonite Chips
		50	32				End of boring at 32 feet	
			33				BACKFILLED BORING TO 28'. INSTALLED 2" DIA. MONITORING WELL	
			34					
			35					
			36					
			37					
			38					
			39					
			40					
			41					
			42					
			43					
			44					
			45					
			46					
			47					
			48					
			49					
			50					
			51					
			52					
			53					
			54					
			55					
			56					
			57					
			58					
			59					
			60					
			61					
			62					
			63					

199503.201709 E:\LOGS\S-KLEEN\RHONERT\DMW-1

SECOR

Reviewed By: _____ Date: _____

Revised By: _____ Date: _____
