SHN CONSULTING ENGINEERS & GEOLOGISTS
812 W. Wabash 707-441-8855
Eureka, CA 95501 707-441-8877

WELLPOINT LOG

ID: SB-2 PAGE 1 OF 1

PROJECT NAME Umpqua Bank
PROJECT NUMBER 004324
LOCATION 409 H St. Eureka
DATE 3/28/05 START 1010 FINISH 1040
DRILLING METHOD DPT
DRILLER Fisch/Rick LOGGED BY EJN

SAMPLER TYPE Macrocore
T.D. OF BORING 14'
T.D. OF WELL 14'
GROUND ELEV.
TOC ELEV.
BOREHOLE DIAMETER 2.25"

LOCATION MAP

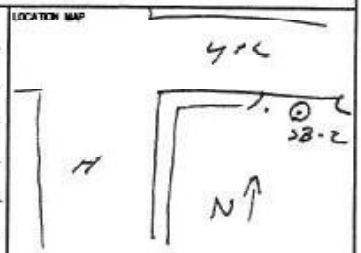

REMARKS	OVA	SAMPLE INTERVAL	% RECOVERY	DEPTH (ft.)	USCS CLASS	LITHOLOGIC DESCRIPTION
			80%	0	SM	Asphalt 0-0.25 silty sand (SM) Brn, M. ~~stiff~~ Dense, Dump, LP, MEK
	0.0		100%	2	ML	sandy silt (ML) Lt. Olv. Brn. (mottled) M. stiff, Dump, LP LEK
	6.0			4	SP/SM	silty sand, Brn, M. Dense Dump, NP, M-HEK.
Sample @ 9.5	0.0			6	SP	sand, Olv Brn, M. Dense moist, NP, HEK
WL @ 9.51				8	SM	silty sand (SM) Olv/Brn mottled, M. Dense, wet, NP HEK
				10		
				12		
				14		
				16		TD @ 14'. 1035/3-28-05

WELLPOINT CONSTRUCTION DETAILS
CASING TYPE/DIA. 3/4" PVC



Casing 0-9'
Screen 9-14

COMMENTS
