SHN CONSULTING ENGINEERS & GEOLOGISTS
812 W. Wabash Eureka, CA 95501 707-441-8855 707-441-8877

WELLPOINT LOG

ID: SB-3 PAGE 1 OF 1

PROJECT NAME: Umpqua Bank
PROJECT NUMBER: 004324
LOCATION: 409 H. Street, Eureka
DATE: 3/28/05 START: 1215 FINISH: 1245
DRILLING METHOD: DPT
DRILLER: Fisch/Rick LOGGED BY: EJN

SAMPLER TYPE: Macrocore
T.D. OF BORING: 13'
T.D. OF WELL: 13'
GROUND ELEV.:
TOC ELEV.:
BOREHOLE DIAMETER: 2.25"

LOCATION MAP

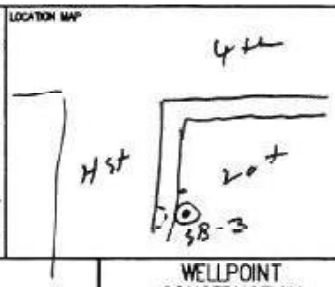

REMARKS	OVA	SAMPLE INTERVAL	% RECOVERY	DEPTH (ft.)	USCS CLASS	LITHOLOGIC DESCRIPTION
			75%	0		Asphalt 0-0.25
				2	ML	Sandy Silt (ML) Brn, M. Stiff Damp, LP, LEK
	0.0		95%	4	SM	Silty Sand (SM) Olv/Brn (mottled) M. Dense, Damp, VLD MEK
	0.0			6		
			95%	8		
Sample @ 9.25 GL @ +9.85				10	SP/SM	Silty Sand (SP/SM) Olv Brn M. Dense, Moist, NP, M-HEK
	0.0			12		Sand (SP) Olv Brn, M. Dense wet, NP, MEK, gravels (11.5-11.0)
				14		Clayey Sand (SC) Brn. M. Dense, wet, LD, M-HEK
				16		TD @ 13' 1245/3-28-05

WELLPOINT CONSTRUCTION DETAILS
CASING TYPE/DIA. 3/4" PVC

Casing 0-8'
Screen 8-13'

COMMENTS
