SECOR

Logged By:	Date:	Contractor:	Project Name:	Method/Equipment:	Log ID:
R. LAPORTE	2/04/05	S & G DRILLING	2885 S. HIGUERA STREET	HOLLOW STEM AUGER CME 75	MW-4

Monitoring Device:	Boring Diameter (in):	Surface Elevation (ft):	Groundwater Depth (ft):	Total Depth (ft):	Drive Weight (lbs):	Drop Distance (in):
PID	8"	NA	NA	20'	140	30"

Abandonment/ Well Construction Details

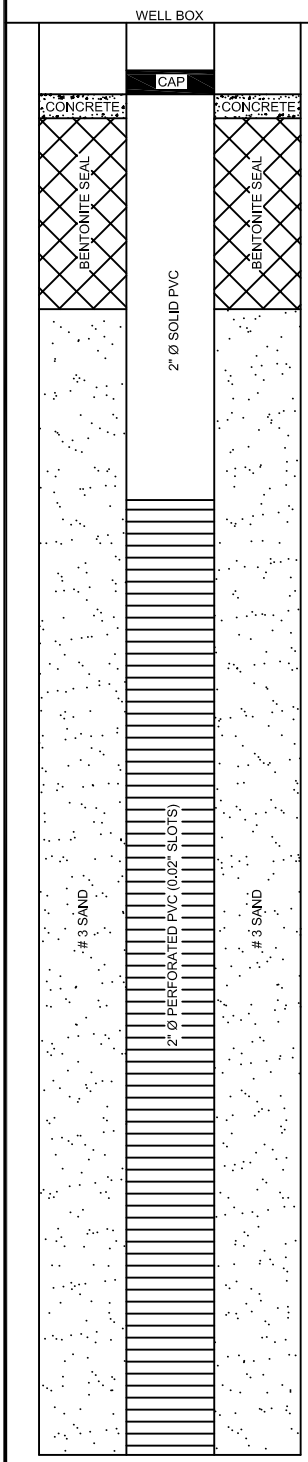

Depth (Feet)	Sample Collected	Blows per 6"	USCS Symbol	LITHOLOGIC DESCRIPTION (**SOIL DESCRIPTION** (USCS symbol): color, moisture, consistency, odor, other)	PID/FID Readings (ppm)	Time Sample Collected
0						
1				**BASEROCK** (GP); light yellow-brown; (fill)		
2				**CLAYEY GRAVEL** (sandstone gravel) (GC); dark brown; moist; (fill)		
3						
4						
5		5				
	X	6		Color change to medium Brown	0.1	14:00
6		8				
7						
8						
9						
10	X	37		**WEATHERED BEDROCK** (Franciscan Formation) (BR); reddish-brown; moist; very dense; fractured	0.1	14:14
		50/4"				
11						
12						
13						
14						
		50/5"			0.1	14:25
15						

SECOR

Logged By:	Date:	Project Name:	Log ID:
R. LAPORTE	2/04/05	2885 S. HIGUERA STREET	MW-4

Abandonment/ Well Construction Details	Depth (Feet)	Sample Collected	Blows per 6"	USCS Symbol	(**SOIL DESCRIPTION** (USCS symbol): color, moisture, consistency, odor, other)	PID/FID Readings (ppm)	Time Sample Collected
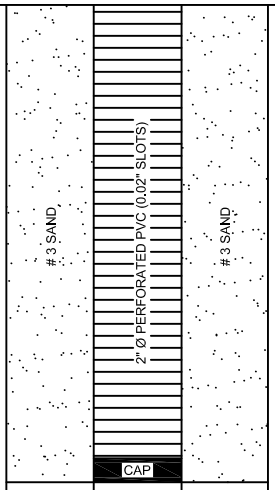	15						
	16						
	17						
	18						
	19		37 50/2"			0.1	14:40
	20				Drilling Terminated		
	21						
	22						
	23						
	24						
	25						
	26						
	27						
	28						
	29						
	30						
