SJN CONSULTING ENGINEERS & GEOLOGISTS
812 W. Wabash Eureka, CA 95501 707-441-8855 707-441-8877

WELLPOINT LOG

ID: SB-4 PAGE 1 OF 1

PROJECT NAME: Umpqua Bank
PROJECT NUMBER: 004324
LOCATION: 409 H
DATE: 3/28/05 START: 1330 FINISH: 1355
DRILLING METHOD: DPT
DRILLER: Fisch / Rick LOGGED BY: SJN

SAMPLER TYPE: Macrocore
T.D. OF BORING: 14'
T.D. OF WELL: 14'
GROUND ELEV.:
TOC ELEV.:
BOREHOLE DIAMETER: 2.25

LOCATION MAP

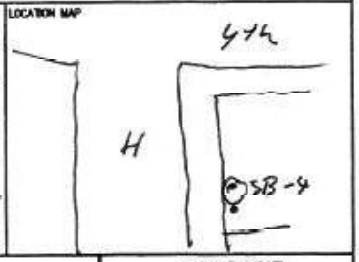

REMARKS	OVA	SAMPLE INTERVAL	% RECOVERY	DEPTH (ft.)	USCS CLASS	LITHOLOGIC DESCRIPTION
			80	0		Asphalt 0-0.25
				2		Sandy silt (ML) Brn, M. Stiff Damp, LP, LEK
	6.0		80	4		Silty Sand (SM) Brn/Olive (mottled) M. Dense, Damp, LP
				6		
	0.0		100	8		Silty Sand (SP/SM) Brn/Olive mottled,
Sample @ 9.5 WL @ 10.03				10	SP	Sand (SP) Lt olive, M. Dense wet, NP, HEK
	0.0		100	12		Silty Sand (SM) Olive Brn/Org Brn mottled, M. Dense, wet, NP HEK
				14		
				16		TD @ 14' - 1355/3-28-05

WELLPOINT CONSTRUCTION DETAILS
CASING TYPE/DIA. 3/4" PVC

Casing 0'-9'
Screen 9'-14'

COMMENTS
